

FUNCTIONAL REQUIREMENT DOCUMENT

Project: PPS Analytics Platform for Gastroenterology

Author: Diwakar Singh

Date: 07-JAN-2021

Version Number – 1.0

DOCUMENT REVISION LIST

SL NO.	VERSION NO.	CHANGES	PAGE NO.	DATE
1	1.0	Initial draft of functional and Non-Functional Requirements	NA	7th Jan 2021

TABLE OF CONTENTS

Project Overview	6
Business Objectives	6
Project Scope	6
Project In Scope.....	6
Project Out of Scope	7
Use Case Diagram.....	8
Project Stakeholders	8
Functional Requirements.....	9
Data Integration and Management.....	9
Patient Stratification and Management	9
Reporting and Analytics	9
Advanced Data Analytics	10
Clinical Decision Support	10
User-Defined Alerts.....	10
Seamless Data Import/Export	10

Customizable Dashboards	10
Appointment Scheduling and Management	10
Patient Communication Portal	11
Audit Trails	11
Use Case – Functional Requirements	11
Use Case 1: Manage Patient Profiles.....	11
Use Case 2: Generate Reports	12
Non-Functional Requirements	13
System Availability	13
Scalability	13
Interoperability	13
Data Security.....	13
Performance.....	13
Usability.....	13
Backup and Disaster Recovery	14
Maintenance and Support.....	14
Use Case – Non-Functional Requirements	14
Use Case 3: System Availability	14
Use Case 4: Data Security.....	15
Use Case 5: Performance	16
Business Process Flow Diagram.....	17
Data Flow Diagram	18
Entity Relationship Diagram	19
Class Diagram	19
Wireframes.....	20
Project Assumptions	25
Project Dependencies	26
Project Risks	27
Data Integration Complexity	27

Regulatory Compliance Failures.....	28
Technology Adoption Resistance.....	28
Budget Overruns	28
Vendor Dependence	29
Project Issues	29
Data Quality Issues	29
Technical Skill Gaps	29
Stakeholder Misalignment	30
Scalability Concerns	30
Delayed Deliverables	30
Project Acceptance Criteria	31
Data Integration and Management.....	31
Patient Stratification	31
Advanced Data Analytics	31
Clinical Decision Support	32
User-Defined Alerts.....	32
Reporting and Analytics Dashboard	32
Security and Compliance.....	32
System Performance and Scalability	33
Glossary	33

Project Overview

The PPS Analytics Platform for Gastroenterology aims to provide GastroGPO and Gastrologix members with advanced analytical tools to improve patient management by leveraging data-driven insights. The platform will enable efficient patient stratification, adherence to clinical pathways, and enhanced decision-making capabilities, ultimately contributing to both clinical and economic value.

Business Objectives

- **Improve Patient Outcomes:** Utilize data analytics to enhance diagnostic accuracy and treatment effectiveness.
- **Increase Operational Efficiency:** Streamline patient management processes to reduce wait times and improve service delivery.
- **Enhance Decision-Making:** Provide real-time, actionable insights to clinicians for better adherence to clinical guidelines.

Project Scope

Project In Scope


1. Data integration from EHRs
2. Patient management systems

3. Billing information
4. Development of analytics modules for risk assessment and treatment optimization
5. User interface for real-time data interaction.

Project Out of Scope

1. Data sources outside of the agreed-upon health systems and databases
2. Legacy system replacement.

Use Case Diagram

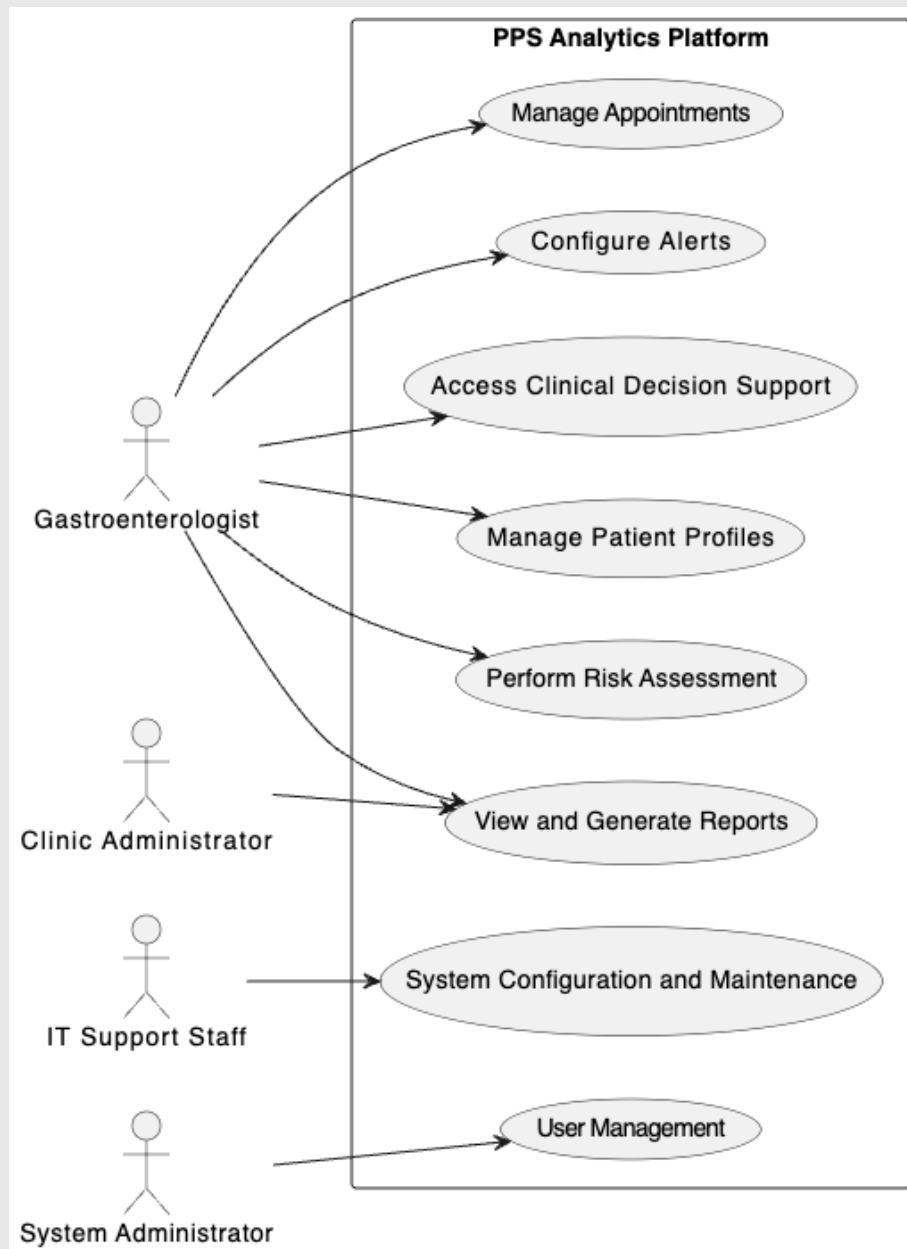

Project Stakeholders

Name	Department	Role
John	Gastroenterologists	Primary users of the platform.
Smith	Clinic Administrators	Secondary users focusing on operational analytics.
Senthil	IT Lead	Responsible for the technical deployment and maintenance
Sagar	Project Management	Project Manager
Amit Patel	Business Analyst	To do Business Analysis

Functional Requirements

Data Integration and Management

- Ability to integrate data from multiple sources with varying formats (e.g., CSV, PDF, HL7)
- Automated data cleansing and preparation for analysis.

Patient Stratification and Management

- Dynamic tools for creating and adjusting patient groups based on multiple criteria.
- Visualization tools for tracking patient progress and outcomes.

Reporting and Analytics

- Customizable dashboards with real-time data updates.

- Reports on adherence to clinical pathways and treatment outcomes.

Advanced Data Analytics

The platform must provide advanced analytics capabilities, including predictive modeling and risk assessment algorithms, to identify patients at high risk of gastroenterological diseases.

Clinical Decision Support

Implement clinical decision support systems (CDSS) that offer treatment recommendations based on the latest clinical guidelines and individual patient data.

User-Defined Alerts

Enable users to configure alerts based on specific criteria such as deviations from treatment protocols or critical patient conditions.

Seamless Data Import/Export

Provide functionality for easy import and export of data in various formats (e.g., CSV, PDF, HL7) to facilitate interoperability with other health systems.

Customizable Dashboards

Users should be able to customize dashboards to display relevant metrics and data points critical to their specific roles and needs.

Appointment Scheduling and Management

Include features for scheduling, rescheduling, and managing patient appointments directly through the platform, including integration with calendar applications.

Patient Communication Portal

Facilitate direct communication channels within the platform for healthcare providers to connect with patients via secure messaging or telehealth features.

Audit Trails

The system must automatically log all user actions and data changes to ensure traceability and compliance with healthcare regulations.

Use Case – Functional Requirements

Use Case 1: Manage Patient Profiles

- Actor: Gastroenterologist
- Goal: To update and retrieve patient profiles.
- Preconditions: User is authenticated.
- Main Flow:
 - a. The gastroenterologist logs into the system.
 - b. The gastroenterologist selects the patient management option.
 - c. The system displays a list of patients.
 - d. The gastroenterologist selects a patient to view detailed information.
 - e. The system displays the patient's profile including medical history, recent visits, and treatment plans.
 - f. The gastroenterologist updates necessary information and submits changes.

- g. The system validates and saves the updates.
- Postconditions: Patient profile is updated in the database.
- Exception Paths: If data validation fails, the system shows an error and requests correct data.

Use Case 2: Generate Reports

- Actor: Clinic Administrator
- Goal: To generate customizable reports on clinic operations and patient health outcomes.
- Preconditions: User must be logged in with administrative privileges.
- Main Flow:
 - h. The administrator accesses the reporting module.
 - i. The administrator selects the type of report from predefined templates (e.g., patient outcomes, clinic efficiency).
 - j. The administrator sets parameters and filters for the report.
 - k. The system processes the request and generates the report.
 - l. The system displays the completed report.
 - m. The administrator downloads or prints the report.
- Postconditions: A report is generated based on specified parameters.
- Exception Paths: If the report cannot be generated (e.g., due to a lack of data), the system displays an error message.

Non-Functional Requirements

System Availability

The platform should be available 24/7, with a downtime of less than 0.1% annually, excluding scheduled maintenance.

Scalability

The system must be scalable to accommodate increasing amounts of data and growing numbers of users without degradation in performance.

Interoperability

Must be compliant with healthcare data exchange standards such as FHIR (Fast Healthcare Interoperability Resources) and HL7 to ensure it can operate within the broader healthcare ecosystem.

Data Security

Implement robust security measures including data encryption at rest and in transit, role-based access control, and regular security audits to protect sensitive patient information.

Performance

Response times for loading data and executing queries should not exceed 3 seconds, ensuring that users experience minimal delay during their interactions with the platform.

Usability

The user interface should be intuitive and accessible, requiring minimal training for users with basic technical skills. It should also be compliant with ADA (Americans with Disabilities Act) standards to ensure accessibility.

Backup and Disaster Recovery

Regular backups of all data must be performed, and a comprehensive disaster recovery plan must be in place to ensure data can be restored quickly in the event of a system failure or other catastrophic events.

Maintenance and Support

Provide ongoing maintenance and technical support to address issues, perform upgrades, and ensure the system operates smoothly over time. This support should be accessible 24/7 to handle critical issues.

Use Case – Non-Functional Requirements

Use Case 3: System Availability

Actor: IT Support Staff

Goal: Ensure system availability meets predefined standards.

Preconditions: None

Main Flow:

- The system is monitored 24/7.
- Automated alerts notify IT staff if system availability drops below 99.9%.

- IT staff investigates and resolves any issues causing downtime.

Postconditions: System maintains at least 99.9% uptime.

Exception Paths: Continuous downtime leads to an escalation procedure with additional IT resources allocated.

Use Case 4: Data Security

Actor: System Administrator

Goal: To ensure all patient data is securely stored and accessed.

Preconditions: Data exists within the system.

Main Flow:

- All data transfers are encrypted using industry-standard protocols.
- System performs regular security audits.
- The System Administrator reviews audit results and adjusts security policies as necessary.
- Any data breach is immediately contained and reported according to regulatory requirements.

Postconditions: Data remains secure, with breaches managed according to policy.

Exception Paths: Failure to comply with security policies results in review and potential system overhaul.

Use Case 5: Performance

Actor: IT Support Staff

Goal: Maintain system performance to meet user expectations.

Preconditions: System is operational.


Main Flow:

- The system is tested under load conditions to ensure response times are within acceptable limits.
- Performance metrics are continuously monitored.
- Any performance degradation triggers an alert to IT support staff.
- IT staff investigates and resolves performance issues, possibly scaling up resources.


Postconditions: System performs within the defined thresholds.

Exception Paths: Ongoing performance issues lead to a system review and potential upgrades.


Business Process Flow Diagram

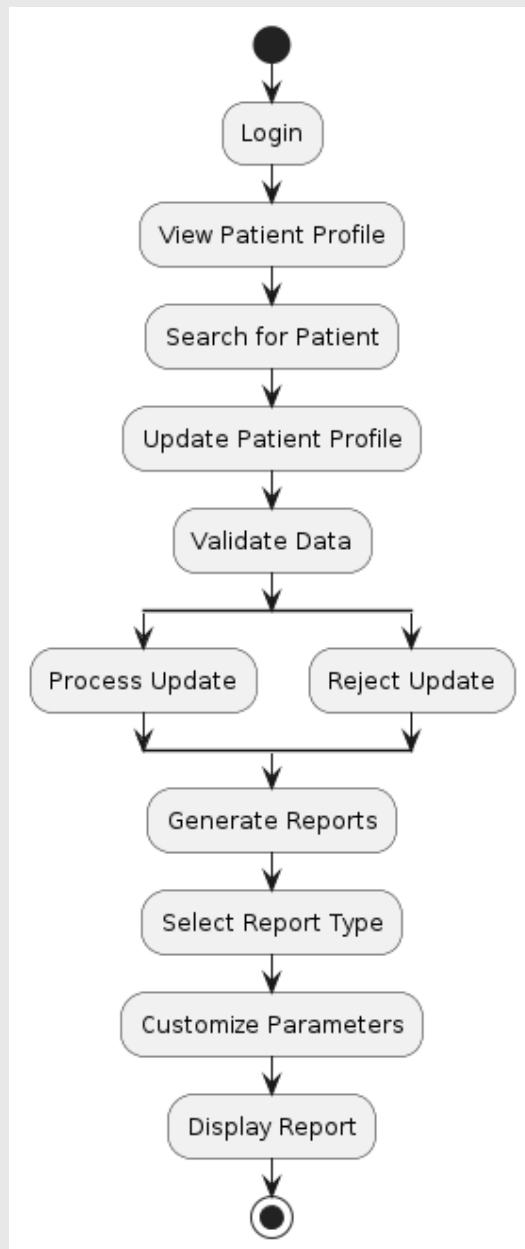


Data Flow Diagram

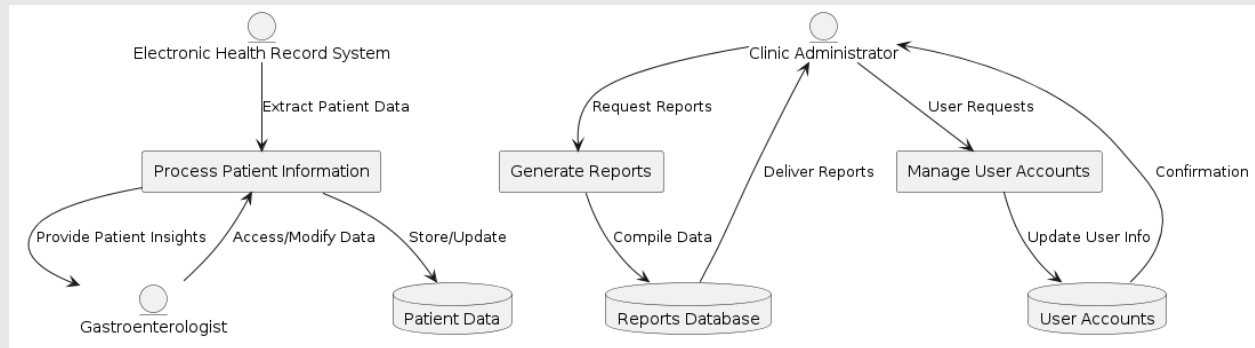

Entity Relationship Diagram

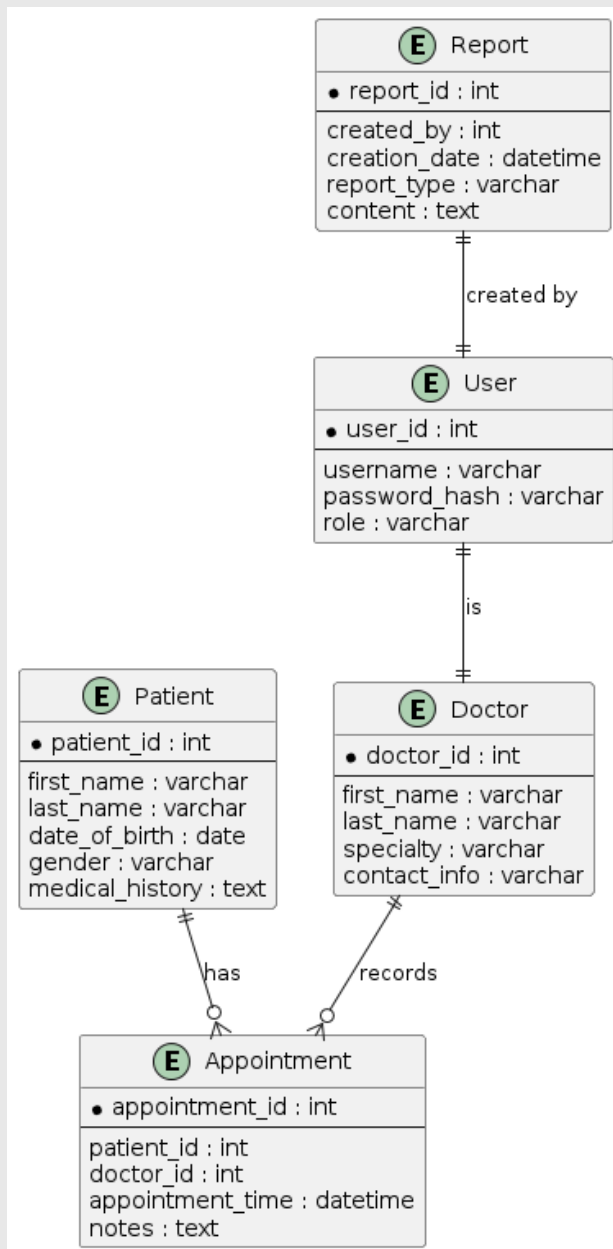

Class Diagram

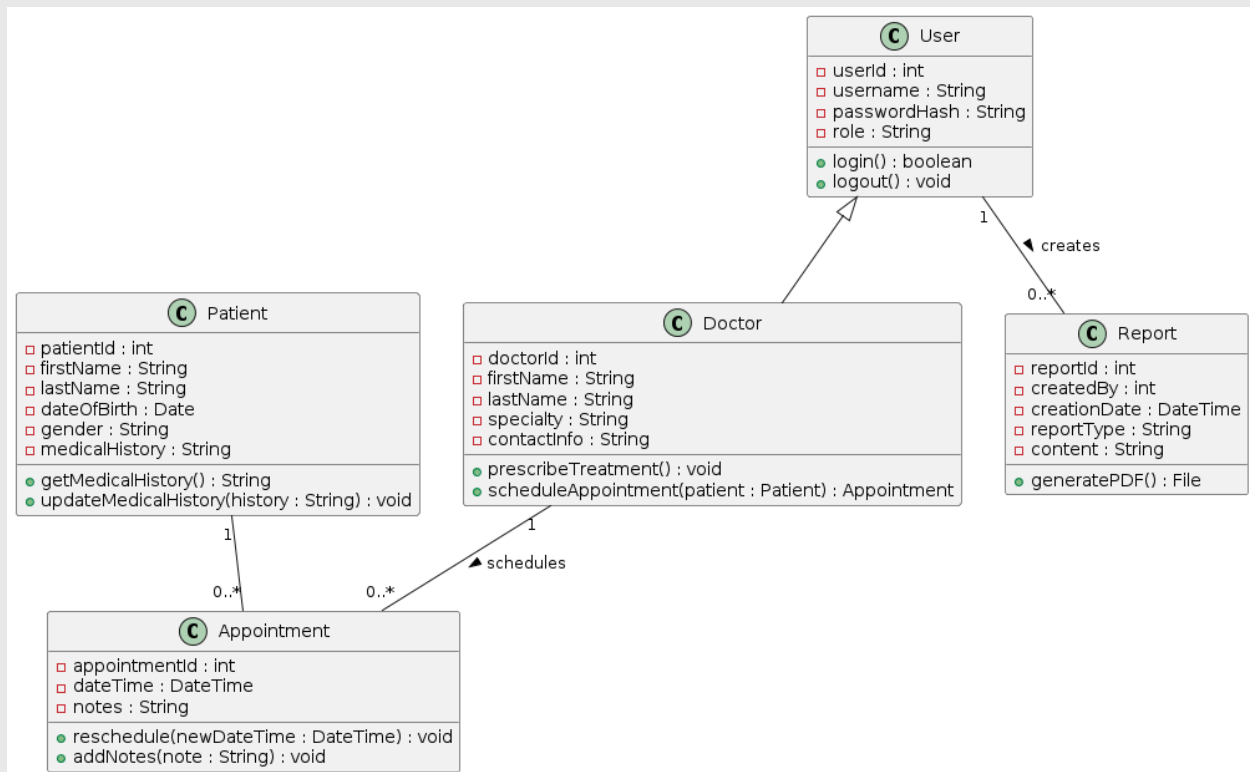


Wireframes

use code GASTROSHIP for free shipping on orders \$100+




Advanced Analytics
Platform




welcome to GastroAnalytics

Empowering GastroGPO and Gastrologix
members with advanced analytical tools for
data-driven patient management.


Explore now



Patient Data




Detailed

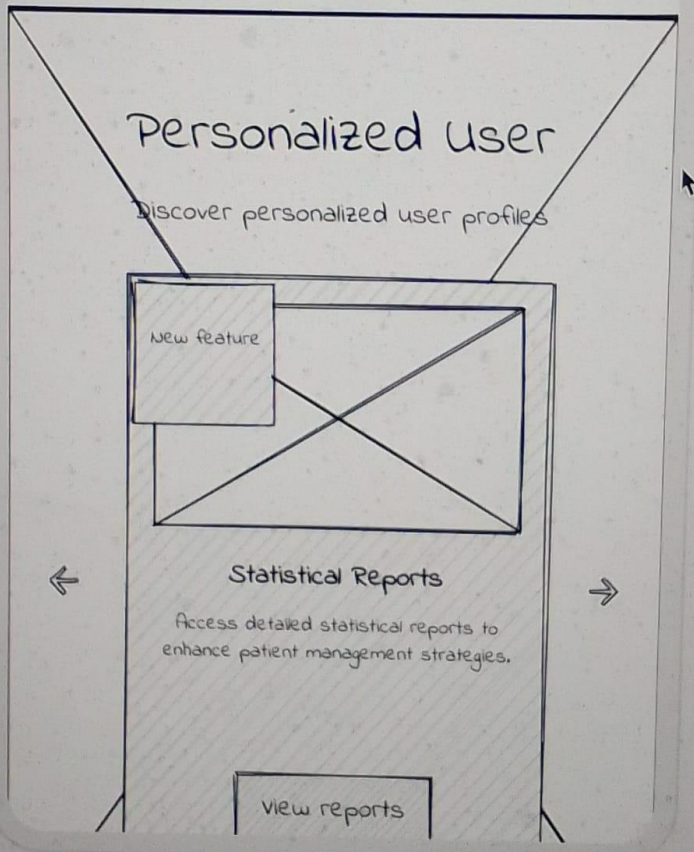


Join GastroAnalytics


Unlock the power of data-driven insights. Join now and access personalized analytics tools.



Search
patient data



Analyze
trends



Generate
reports

Join now


Manage your subscription preferences

Popular Analytics Tools

Popular Analytics Tools

Explore our best-in-class analytics tools and optimize patient management with data-driven insights.

Explore tools




try dem

Data Analysis Tool

Advanced data analysis



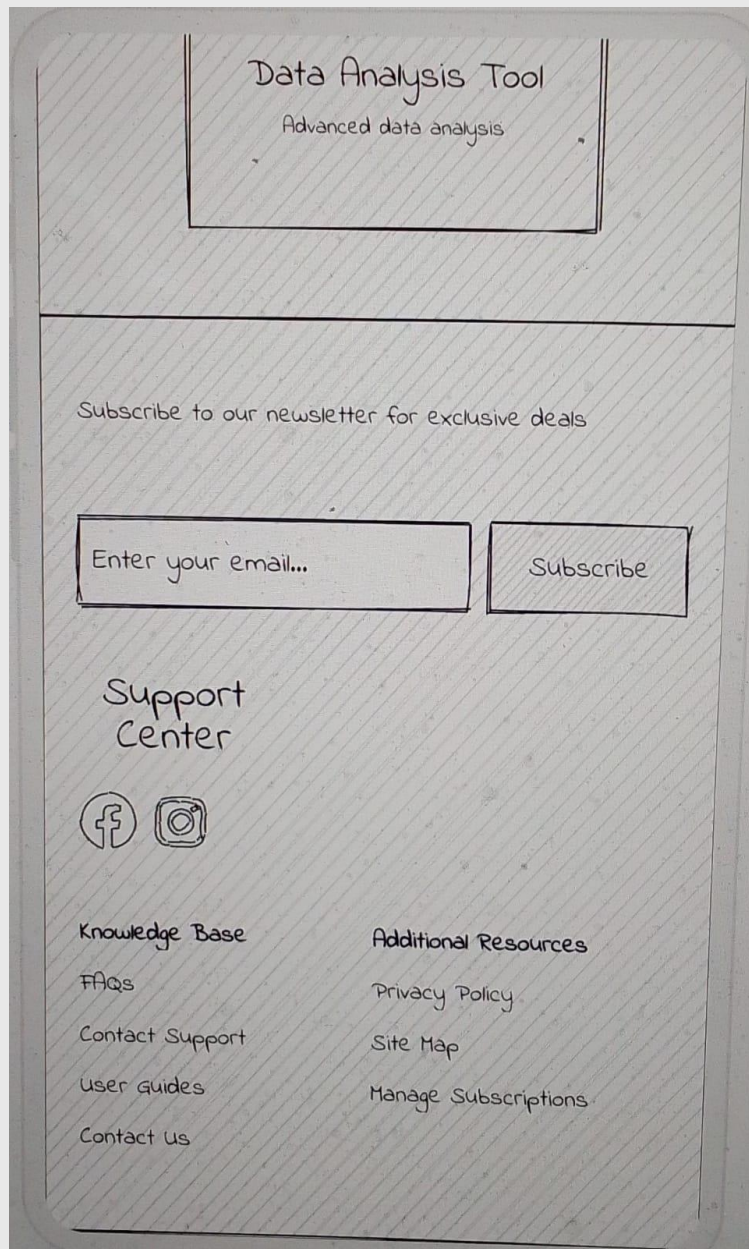

Project Assumptions

- Stable integration capabilities with existing EHR systems without significant upgrades.
- It is assumed that gastroenterologists and clinic administrators have basic proficiency with digital health tools,

which will minimize the training required to use the new platform.

- The success of the platform is predicated on the assumption that the data being integrated from existing sources like EHRs, and patient management systems is of high quality, accurate, and up to date.
- The healthcare facilities where the platform will be deployed are assumed to have the necessary technology infrastructure, including reliable internet access and hardware capable of running the platform efficiently.
- All data integration and handling processes are assumed to comply with existing healthcare regulations and data protection laws without requiring additional legal scrutiny.
- It is assumed that any third-party vendors or software providers involved in the project will continue to provide stable support and service throughout the platform's development and deployment phases.
- The healthcare staff at participating facilities are assumed to be receptive to adopting new technologies and will engage positively with the change management process introduced by the platform's implementation.

Project Dependencies

- The project's timeline and success depend on the ability to integrate seamlessly with multiple existing data systems and

software, which may require cooperation from various software vendors and IT departments.

- Key stakeholder availability for crucial meetings, feedback sessions, and training workshops is a critical dependency. Delays in stakeholder engagement can lead to project delays.
- The project depends on obtaining necessary regulatory approvals for data handling and processing, which might involve audits and inspections from data protection authorities.
- Successful data migration from existing systems to the new platform is a dependency that involves risks related to data loss or corruption during transfer.
- Continuous financial support and budget approval from the healthcare facilities' administration are crucial. Any cuts or delays in funding can significantly impact project timelines and scope.
- External factors such as changes in healthcare policies, market dynamics, and economic stability are dependencies that could impact project execution and outcomes.

Project Risks

Data Integration Complexity

Risk: Challenges in integrating disparate data sources could lead to delays and increased costs.

Mitigation: Implement a pilot program to identify potential integration issues early. Engage experienced data integration specialists and use middleware solutions to streamline the process.

Regulatory Compliance Failures

Risk: Failure to comply with healthcare regulations like HIPAA could result in legal penalties and damage to reputation.

Mitigation: Conduct regular compliance audits and engage legal experts to review project practices. Implement strict data security measures and continuous monitoring.

Technology Adoption Resistance

Risk: Resistance from users due to unfamiliarity with new technology could hinder the platform's adoption and effectiveness.

Mitigation: Develop comprehensive training programs and provide continuous support. Involve end-users early in the design process to ensure the platform meets their needs and preferences.

Budget Overruns

Risk: Project costs may exceed initial estimates due to unforeseen technical challenges or scope changes.

Mitigation: Implement strict budget management procedures, regularly review financial performance, and maintain a contingency reserve.

Vendor Dependence

Risk: Over-reliance on third-party vendors for critical software components could lead to issues if vendors fail to deliver as promised.

Mitigation: Diversify vendor options, establish clear contractual agreements with performance clauses, and maintain an active vendor management strategy.

Project Issues

Data Quality Issues

Issue: Initial data collected from various sources may have inconsistencies and inaccuracies that affect platform reliability.

Resolution: Implement robust data cleaning and validation processes. Regularly update these processes as more data is integrated.

Technical Skill Gaps

Issue: The project team may lack certain technical skills required for advanced data analytics and platform development.

Resolution: Identify skill gaps early and consider hiring new talent or offering training to existing staff. Outsourcing can also be an option for highly specialized skills.

Stakeholder Misalignment

Issue: Conflicting priorities among stakeholders can lead to disagreements on the project's direction.

Resolution: Regularly engage all stakeholders through meetings and updates to align on goals and expectations. Use conflict resolution strategies and compromise where necessary.

Scalability Concerns

Issue: The platform may not be able to handle the increasing load as more users and data are added, leading to performance degradation.

Resolution: Design the platform with scalability in mind from the start. Regularly perform load testing and plan for infrastructure upgrades as necessary.

Delayed Deliverables

Issue: Project timelines may be extended due to technical setbacks or external factors such as regulatory changes.

Resolution: Implement agile project management methodologies to adapt to changes rapidly. Keep a flexible project timeline with buffer periods for critical tasks.

Project Acceptance Criteria

Data Integration and Management

- The system must integrate data from at least three different sources (EHRs, patient management systems, lab results).
- Data integration processes must be completed within 5 minutes for daily updates consisting of up to 10,000 records.
- No more than 0.01% error rate in data integration.

Patient Stratification

- Users must be able to create and modify patient groups based on at least five different criteria (e.g., age, diagnosis, treatment history, risk factors).
- The system must update patient groups in real-time as new data becomes available.
- The stratification tool must handle up to 100,000 patient records without performance degradation.

Advanced Data Analytics

- Predictive models must achieve a minimum accuracy of 90% in identifying high-risk patients as validated by retrospective data.
- Reports generated by the analytics module should load within 3 seconds.
- Users must be able to customize analytics parameters through a user-friendly interface.

Clinical Decision Support

- The system must provide at least three treatment recommendations based on current clinical guidelines.
- Decision support prompts must be triggered within 1 second of relevant data entry or update.
- Users must be able to override or ignore recommendations with documented reasons.

User-Defined Alerts

- Alerts must be configurable for a variety of parameters, including lab results out of expected range and missed appointments.
- Alerts must be delivered to the designated healthcare provider's interface within 10 seconds of the triggering event.
- Users must be able to acknowledge or act on alerts directly from the notification pane.

Reporting and Analytics Dashboard

- Dashboards must refresh with updated data every 5 minutes automatically.
- Users must be able to access historical data and trends for up to 5 years.
- Export of data from dashboards to PDF or Excel should not exceed 10 seconds.

Security and Compliance

- The platform must pass a third-party security audit without critical findings.
- Role-based access controls must enforce that users can only access data and functionalities specific to their roles.
- All access and changes to sensitive data must be logged and retrievable for at least 6 years.

System Performance and Scalability

- The platform must support simultaneous use by up to 500 users without core functionalities slowing down by more than 10% compared to baseline.
- Scalability testing must show that adding additional data or users does not decrease system performance linearly.

Glossary

Analytics Module

Definition: A component of the platform that processes data to generate insights, including predictive analytics and reporting functionalities.

Clinical Decision Support System (CDSS)

Definition: An integrated system within the platform that uses patient data to provide treatment recommendations based on clinical guidelines.

Data Integration

Definition: The process of combining data from different sources into a single, unified view to enable more effective and coherent analysis.

Electronic Health Records (EHRs)

Definition: Digital versions of patients' medical histories that are maintained by the provider over time, including diagnostics, treatments, and clinical notes.

Extract, Transform, Load (ETL)

Definition: A process in database usage and data warehousing that involves extracting data from outside sources, transforming it to fit operational needs, and loading it into the end target (database or data warehouse).

FHIR (Fast Healthcare Interoperability Resources)

Definition: A standard describing data formats and elements (known as "resources") and an application programming interface (API) for exchanging electronic health records.

GastroGPO

Definition: A group purchasing organization specifically for gastroenterology practices, aimed at leveraging purchasing power to obtain discounts from vendors based on the collective buying power of its members.

Gastrologix

Definition: A cooperative that works with independent gastroenterology practices to manage their operations, including financial and patient care optimization.

HIPAA (Health Insurance Portability and Accountability Act)

Definition: U.S. legislation that provides data privacy and security provisions for safeguarding medical information.

Patient Management System

Definition: Software used by healthcare providers to manage information related to patient care, including scheduling, billing, and other administrative tasks.

Patient Stratification

Definition: The process of segmenting patients into various groups based on predefined criteria such as risk or diagnosis to tailor care approaches effectively.

Predictive Modeling

Definition: A process that uses data and statistical algorithms to predict outcomes with significant accuracy within a model.

Role-Based Access Control (RBAC)

Definition: A method of restricting system access to authorized users based on their roles and responsibilities within the organization.

User Interface (UI)

Definition: The means by which the user and a computer system interact, particularly the use of input devices and software.

User Acceptance Testing (UAT)

Definition: The process of verifying that a solution works for the user and meets all their requirements in a real-world scenario.
